

Monthly Status Briefing

October 2013



Pueblo Chemical Agent-Destruction Pilot Plant



Program Executive Office
Assembled Chemical Weapons Alternatives



PCAPP

Pueblo Chemical Agent-Destruction Pilot Plant

www.peoacwa.army.mil




A PARTNERSHIP FOR SAFE CHEMICAL WEAPONS DESTRUCTION

Project Background



The Program Executive Officer, Assembled Chemical Weapons Alternatives (ACWA), headquartered at Aberdeen Proving Ground, Maryland, is responsible for managing all aspects of the safe and environmentally sound destruction of the chemical weapons stockpiles in Colorado and Kentucky.



Pueblo Chemical Agent-
Destruction Pilot Plant

The Pueblo Chemical Agent-Destruction Pilot Plant (PCAPP) will safely destroy 2,611 tons of mustard agent in mortar rounds and artillery projectiles stored at the U.S. Army Pueblo Chemical Depot (PCD).

- Neutralization followed by biotreatment is the technology selected by the Department of Defense to destroy the Pueblo chemical weapons stockpile.



The Bechtel Pueblo Team (BPT) is a partnership of Bechtel National, Inc., URS, Parsons, and Battelle Memorial Institute. The BPT functions as the systems contractor selected to design, build, systemize, pilot test, operate, and close the PCAPP.





- Bechtel Pueblo Team non-manual: **842**
 - Pueblo: 840
 - Pueblo County local hires: 197
 - Colorado hires (outside Pueblo County): 43
 - Other locations: 2
- Construction Workers: **179**
 - Bechtel direct-hire craft workers: 110
 - Subcontractor personnel: 69

Employment Opportunities

Hotline

(719)549-4003

Website

<http://pueblo.bechtel.com>



As of September 30, 2013,
PCAPP Project staff accomplished:

- 522 Safe Work Days*
- 2,748,740 Safe Work Hours



* Last Lost Time occurred on April 26, 2012

Step 1



Removal of Energetics

Robotic equipment removes energetics (explosives) from the weapon. The energetics will be disposed of at a permitted facility offsite.

Step 2



Removal of Mustard Agent

The inside of the weapon is remotely accessed and mustard agent is washed out with high-pressure water.

Step 3



Neutralization of Mustard Agent

The mustard agent is neutralized with caustic solution and hot water. The byproduct is called hydrolysate.

Step 4



Biotreatment

Microbes treat the hydrolysate, breaking it down into brine. The brine is separated with water being recycled back to the plant and salt cakes shipped for disposal at a permitted facility.

Step 5




Thermal Treatment and Disposal of Metal Parts

Metal Parts are heated to 1,000 degrees Fahrenheit for 15 minutes and can then be recycled.

Neutralization followed by biotreatment will be used to destroy the Colorado chemical weapons stockpile.

Pueblo Chemical Agent-Destruction Pilot Plant—Site Plan

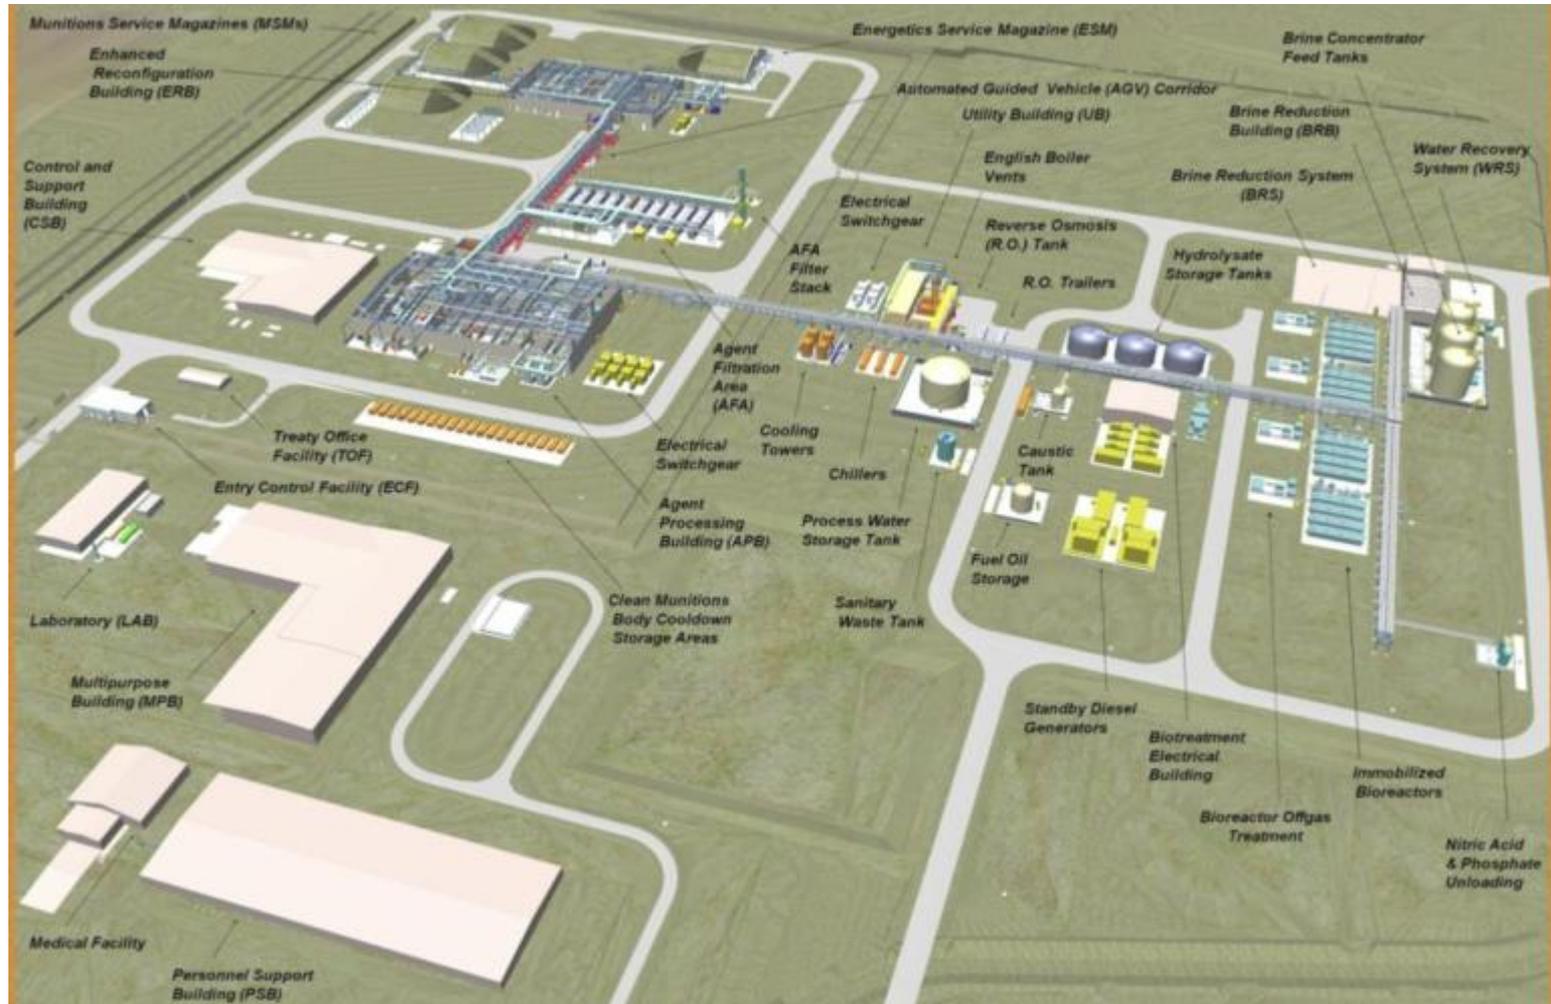

PCAPP Site Overview



Northwestern Corner - Observation Point

- | | | | |
|----------|--|----------|--|
| 1 | Enhanced Reconfiguration Building | 5 | Agent Filtration Area |
| 2 | Automated Guided Vehicle Corridor | 6 | Munitions Service Magazine |
| 3 | Agent Processing Building | 7 | Control and Support Building |
| 4 | Biotreatment Area | 8 | Munitions Service Magazine Corridor |

As the project transitions from construction to systemization, the following systems have been turned over to the start-up group to begin the systemization process:

- Agent Collection and Neutralization System—Hydrolysate Collection and Storage—Yard
- Breathing Air—A & B Compressor/Purifier Packages, Receiver and Chiller, Bottle Filling Station, Supply and Change Stations
- Enhanced Reconfiguration Building (ERB) HVAC: Supply Air Handling Units/Control Room and Support Areas Ventilation System; ERB Cascade Ventilation System; Electrical Room Ventilation System
- Steam Supply—Fuel Oil Piping, Natural Gas Piping, Amine Feed Skid, Boilers A & B and Outside Rack Steam; Agent Processing Building (APB)/Biotreatment Area (BTA)/Brine Reduction System (BRS) Distribution
- Bulk Chemical Storage and Distribution—DAP, UREA and 25% caustic
- Projectile Handling and Projectile Disassembly—Projectile Mortar Disassembly systems and Related Equipment—Lines 1, 2, and 3; Munitions/Parts Monitoring
- Chilled Water—Chillers, Distribution to various HVAC units, recirculation units, autoclave and Off-Gas Treatment scrubber
- Immobilized Cell Bioreactor (ICB) Feed, Biotreatment, ICB Blower and Off Gas Treatment—Modules 1/2/3/4, Biotreatment Electrical Building
- Process Cooling Water—pumps, tanks, chemical feed skids, cooling towers, BRS Distribution
- Brine Reduction System (BRS)—Brine Concentrator Feed (BCF) Tanks “A”, “B”, and “C” and BCF Tanks Off-Gas Treatment; Brine Reduction Belt Feed System, BRS Filter Press Building, all BRS Electrical Systems



To learn more about Systemization, watch the video at http://www.peoacw.a.army.mil/info/video/systemization_yt.html

Systemization (cont.)

- APB—Munitions Washout System (MWS) Instrument Air Distribution; Process Water Distribution; Hydraulic Power Line 1 & 2; Hot Process Water Tank and Heating Coil; MWS High Pressure Water Supply and Distribution; MWS Drain, Wash and Collection Line 1 & 2; Off-Gas Treatment System; MWS Agent Wash Water Transfer; APB Fire Protection Systems
- APB Decon Storage (SDS) Holding Tanks and Feed Pumps; SDS "A" Sumps; SDS "B" pumps; SDS "C" Pumps
- Munitions Treatment Units #1 and #2; Muniton Body Storage Building—Gravity Conveyors
- APB HVAC: Supply Air Handling Units, Battery Room Ventilation System; Cascade Ventilation System, Operator Work Station Ventilation System, Recirculation Units, Unit Heaters and Ventilators; Electrical Room Ventilation System; Entry Support Area Ventilation System; Electrical Room Ventilation System; Entry Support Area Ventilation System
- Agent Monitoring: Agent Filtration Area; Laboratory, APB, Automated Guided Vehicle (AGV) corridor, ERB
- Facilities: Control Support Building; Medical Building; Laboratory; Utility Building, APB, ERB, AGV corridor, Entry Control Facility, Brine Reduction Filter Building (BRB), Biotreatment Electrical Building
- APB Agent Collection and Neutralization System— Agent Collection; Agent Neutralization; Hydrolysate Collection and Sampling Systems
- Site Security Diesel Generator
- Secondary Waste Treatment: Secondary Decontamination Unit System & Autoclave
- Residue Handling System
- Site Security Essential Power
- Site Grounding System
- Closed Circuit TV (CCTV): APB, ERB, Yard, BTA
- AGVs with maintenance charge



Coatings



Coatings work continues throughout the plant. In the Enhanced Reconfiguration Building's Travelling and Receiving Area, new floor coatings will protect the concrete from any accidental spillage.

Agent Processing Building



Workers apply grout to the bases of the Cavity Access Machines (CAM). The grout will prevent agent accumulation under the units in the event of an accidental spill. The CAMs use a hydraulic ram to collapse burster wells inside the munitions, thereby allowing agent to gravity drain.

Pueblo City Council Tour



PCAPP Project Manager Rick Holmes (right) explains the Agent Filtration Area system to Pueblo City Council members (from left) Sandy Daff, Chris Nicoll, Ed Brown and Ami Nawrocki during a tour of the site on Sept. 19.

PCAPP Job Symposium



A second PCAPP Job Symposium will be held at the Pueblo Convention Center on Nov. 13. Watch for details to be printed in the *Pueblo Chieftain*.

Contact Information



Pueblo Chemical Stockpile Outreach Office

104 West B Street
719-546-0400

Tom Schultz

PCAPP

Public Affairs Specialist

David Ortiz

Public Outreach Manager

Sandy Romero

Bechtel Pueblo Team
Communications Manager

U.S. Army Pueblo Chemical Depot

45825 Highway 96 East
719-549-4135

Chuck Sprague

Public Affairs Officer

Ken Roque

Deputy Public Affairs Officer



Program Executive Office
Assembled Chemical Weapons Alternatives

